


2017 Runway 05/23 Rehabilitation Phases

AVIATION SERVICES RUNWAY 05/23 CLOSURE BASE TIMELINES

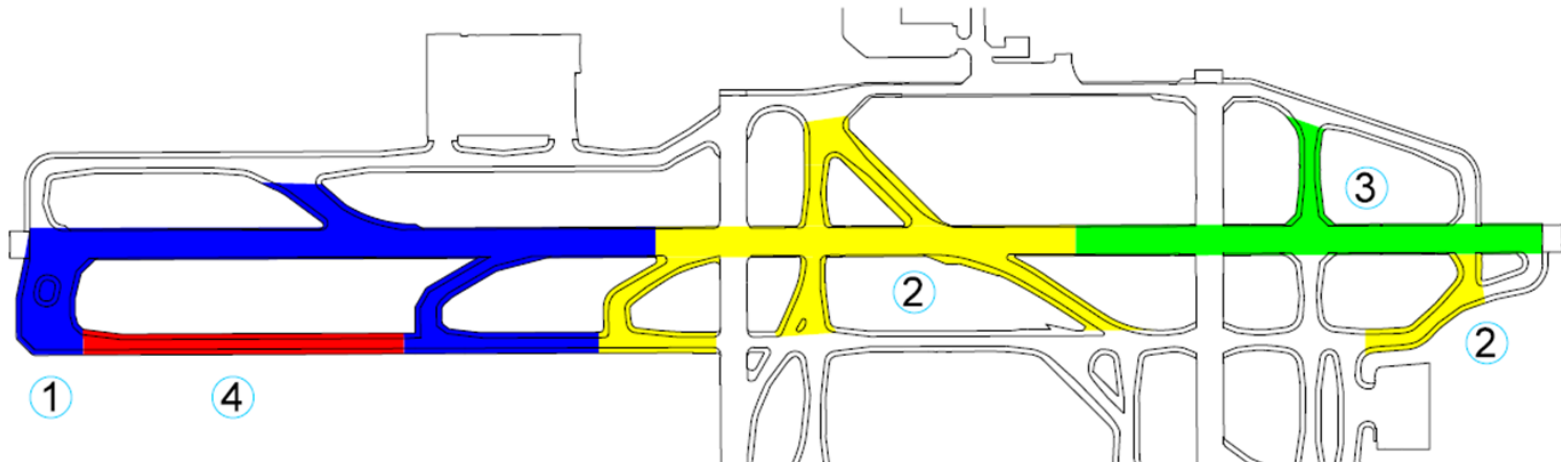

SEGMENT	RWY STATUS	FROM	TO	DAYS
1	SHORT OP FROM H2 [NO ARR 05]	MARCH 28, 2017	APRIL 23, 2017	26
2	CLOSED	APRIL 24, 2017	MAY 16, 2017	22
3*	SHORT OP FROM H3 [NO ARR 23]	OCT 10, 2017 (*April 24, 2017)	NOV 3, 2017 (*May 16, 2017)	21
4*	N/A	Mid-April 2018 (*April 24, 2017)	May 2018 (*May 16, 2017)	TBD

* Decision regarding the feasibility of adding Phases 3&4 to Phase 2 will be made by April 30, 2017. *
